

**NO.NHSRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/ 4701**

**Dated:24/04/2019**

The Project Director,  
Japan International Cooperation Agency,  
JICA India Office,  
16<sup>th</sup> Floor, Hindustan Times House,  
18-20 Kasturba Gandhi Marg,  
New Delhi - 110001

**Sub: RAP Implementation Monitoring Quarterly Progress Report – 2 for  
MAHSR Project.**

**Ref : Annexure M of Minutes of Discussions on Project for the Construction of  
Mumbai-Ahmedabad High Speed Rail (I) and Project for the Construction of  
Mumbai-Ahmedabad High Speed Rail (II) between Japan International  
Cooperation Agency and Ministry of Railways /National High Speed Rail  
Corporation Limited dated 18.09.2018.**

With above reference, NHSRCL would like to inform you that, the second quarterly progress report (1<sup>st</sup> January 2019 – 31<sup>st</sup> March' 2019) of Internal Monitoring of RAP (Resettlement Action Plan) i.e. Annexure M have been prepared by NHSRCL. The same is submitted for your information and necessary action.

  
**(Anjum Pervez)  
Officer on Special Duty**





# QUARTERLY PROGRESS REPORT – II ( JANUARY – MARCH’ 2019)

*RAP Implementation Monitoring Format (Annexure M)*

*for*

*Mumbai – Ahmedabad High Speed Rail Limited*

Submitted by:

NATIONAL HIGH SPEED RAIL CORPORATION LIMITED 2nd FLOOR, ASIA BHAWAN, ROAD NO-205,  
DWARKA SECTOR 9, NEW DELHI – 110077

## Quarterly Progress Report Number 2


**Time-Frame: 1<sup>ST</sup> January' - 31<sup>st</sup> March, 2019**

### **PROJECT AT GLANCE**

The Ministry of Railways formulated the Indian Railways Vision 2020 in December 2009. The vision aims to modernize the existing conventional lines and enhance their traffic capacity as well as develop high-speed railway lines. Seven routes were selected as candidates for the high-speed railway system. Among them, the Mumbai–Ahmedabad route was given top priority by the Experts Committee on Modernization of India’s National Railways established by the Ministry of Railways. Based on this plan, the Mumbai–Ahmedabad High-Speed Railway will be implemented. In this context, Japan and India issued a joint statement in May 2013 committing to conduct a joint study on the Project. Based on this decision, the Joint Feasibility Study for Mumbai–Ahmedabad High-Speed Railway Corridor was conducted from December 2013 to June 2015. Then, the Prime Ministers of Japan and India issued a joint statement in December 2015, agreeing to introduce the Shinkansen High-Speed Railway (HSR) System to the Mumbai Ahmedabad route

**Figure 1: Route of Mumbai–Ahmedabad High-Speed Railway line**

The Mumbai–Ahmedabad High-Speed Railway Line (HSRL) will connect Mumbai, the capital city of Maharashtra and the second most populous metropolitan area in India, with Ahmedabad which is a metropolis in Gujarat. The approximately 508-km-long line will consist of high-speed railway vision running along the Arabian Sea coast and connecting with Surat and Vadodara en route which are the second and third largest city in Gujarat. The alignment will pass through Maharashtra, Gujarat and part in Dadra & Nagar Haveli covering 12 districts. The stretch in Maharashtra is 155.72 km, the stretch in Dadra & Nagar Haveli is 4.3 km and stretch in Gujarat is 348.15 km.

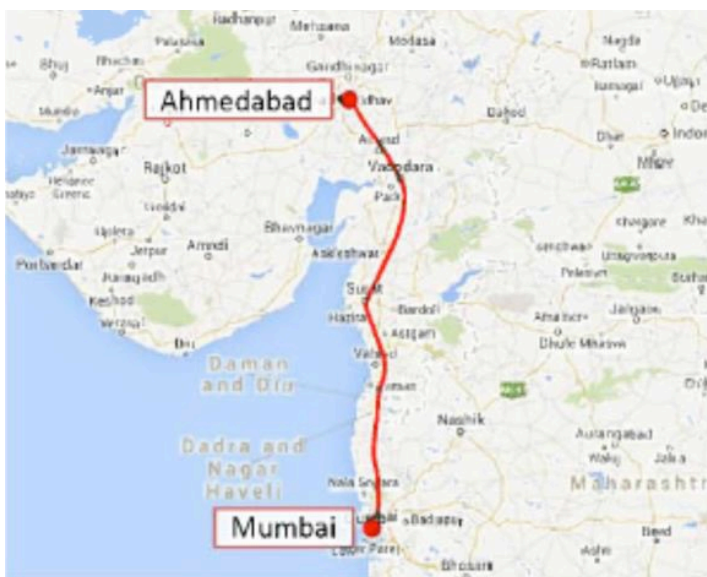

### **1. TOTAL LAND REQUIREMENT FOR THE PROJECT**

In total, 8878 land plots with area comprising 1434.47 ha of land in 297 villages is required for the project. This includes private land, government land, forest land and land of Indian Railways. Around 78.4% of land plots affected are private land and remaining land belongs to Indian Railways, Government land and forest land.

## **2. KEY OBJECTIVE OF RESETTLEMENT ACTION PLAN**

The main objective of the detailed resettlement action plan (RAP) is to ensure that the project design and implementation are socially acceptable based on the JICA Guidelines for Environmental and Social Considerations, 2010<sup>1</sup>. From July, 2017 to July 2018, a Social Impact Assessment Study was done based on which a RAP has been prepared. The RAP is approved by NHRCL as per no. NHRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/2588 dated 12.09.2018. It has identified all potential social issues in the project and has developed mitigating measures for the impact of the project. The total estimated cost of implementing the RAP is ₹14,217.28 crores.

## **3. PROJECT IMPACT**

The project being linear in nature is not expected to result in large-scale displacement of community. Impact on livelihood is mainly due to the acquisition of private agricultural land and business units along the project corridors. District-wise details of Project Impacts are presented in the table below.

SUMMARY OF PROJECT IMPACTS (As per RAP)	
➤	Total Number of Project Affected Household: 14,884
➤	Number of Affected Title Holder: 10,305
➤	Number of Affected Non-Title Holder: 4,579
➤	Total Number of Affected Structures: 3892
➤	Total Number of Affected CPRs: 37
➤	Total Number of Affected Commercial Structures: 271
➤	Total number of Impacted Trees: 37,394

## **4. MONITORING OF RESETTLEMENT ACTION PLAN**

From July, 2017 to July 2018, a Social Impact Assessment Study was done based on which a RAP has been prepared. The RAP is approved by NHRCL as per no. NHRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/2588 dated 12.09.2018. It has identified all potential social issues in the project and has developed mitigating measures for the impact of the project. The total estimated cost of implementing the RAP is ₹14,217.28 crores.

NHRCL is submitting the second quarterly progress report to JICA for the period of January 1<sup>st</sup>, 2019 to March 31<sup>st</sup>, 2019.

<sup>1</sup> [https://www.jica.go.jp/english/our\\_work/social\\_environmental/guideline/pdf/guideline100326.pdf](https://www.jica.go.jp/english/our_work/social_environmental/guideline/pdf/guideline100326.pdf)

## KEY HIGHLIGHTS OF THIS QUARTER

1. **Engagement of Staff for RAP Implementation:** NHSRCL has engaged human resources to cover this aspect at all three levels- Headquarters, Districts and Villages.

a. NHSRCL's senior management along with Social Development Officer and Assistant Social Development Officer is in charge of matters at Headquarter level.

i. Managing Director	- 1
ii. Director (Projects)	- 1
iii. Officer on Special Duty	- 1
iv. Social Development Officer	- 1
v. Assistant Social Development Officer	- 1
vi. Project Managers (Civil)	- 1
vii. Project Managers (QAQC)	- 1

b. At the site 5 Chief Project Managers at Ahmedabad, Vadodara, Surat, Palghar and Mumbai are managing land acquisition and Resettlement Action Plan implementation related issues in Gujarat, Dadar & Nagar Haveli and Maharashtra. The details of staff deployed is given below.

S. No.	District	NHSRCL			
		DILR/LAO's Office	Communicators	NHSRCL's Staff	
				Permanent	Temporary/ Out-sourced Staff/Revenue
1	MUMBAI SUBURBAN	0	0	0	0
2	THANE	11	7	3	11
3a)	PALGHAR	29	30	9	19
3b)	PALGHAR (For VDP)	0	0	0	9
4	DNH	0	0	0	1
5	VALSAD	6	17	3	7
6	NAVSARI	3	0	0	0
7	SURAT	8	8	2	6
8	BHARUCH	8	16	3	4
9	VADODARA	25	9	2	13
10	ANAND	7	4	1	4
11	KHEDA	8	5	1	8
12	AHMEDABAD	7	4	3	6
	<b>Total</b>	<b>112</b>	<b>100</b>	<b>27</b>	<b>88</b>

c. There is a deployment of 79 manpower to ensure effective implementation of RAP. Through RAP implementing agency i.e. M/s Arcadis about 52 manpower has been deployed for land acquisition and social safeguard activities. Further, additional deployment of about 27 manpower has also been done by engaging two agencies i.e. CPMA and RANE for Information Education and Communication activities in Palghar district.

*Details Provided in Row 1 of Attachment M*

2. **Progress of Joint Measurement Survey:** Out of total **297 villages** falling in the project alignment, field-work for JMS has been completed in **245 villages**. This is around 82 percent of the total villages. The other steps involved include preparation of Joint Measurement Reports for the villages, submission to district authorities and subsequent approval. **Approximately 79% of the Joint Measurement Reports** submitted to district administration have been approved by Land Acquisition Officer. Efforts are in place to expedite the process to complete the remaining stretch of JMS.

*Details Provided in Row 2 of Attachment M*

3. **Valuation of Properties attached to the structure:** Valuation has to be done for structures, trees and utilities attached to the land being acquired. After confirmation on numbers in Joint Measurement Report, the values of the structure is calculated by government authorized valuer. The details are further confirmed by Road & Building Department in Gujarat and Public Works Department in Maharashtra and DNH.

**Approximately, 60% valuation is complete for structures.** NHSRCL is following up with respective state government and administration of Union Territory to speed up the process, regular follow-up meetings are held with State Government officials at different level in this regard.

*Details Provided in Row 3 of Attachment M*

4. **Verification of Impacts after completion of JMS** NHSRCL created a software for Management Information System in March, 2019. After Joint Measurement Reports for the villages are finalized by the district administration, the complete details are filled in the software. While 14884 households were identified at the time of socio-economic survey during RAP, for the villages where JMS have been completed & JMR are received, the number of Project Affected Households are 9242 and corresponding number of project affected persons identified are 42002.

*Details Provided in Row 4 of Attachment M*

5. **Adopting the RAP** RAP has been summarized and translated into Gujarati and Marathi in Dec, 2018 and the same has also been uploaded in NHSRCL Website. NHSRCL plans to submit this copy to all land acquisition officers. Further, communication campaigns are also been organized for Project Affected Persons (PAP).

*Details Provided in Row 5 of Attachment M*

6. **Progress of Land Acquisition** At present, NHSRCL is acquiring land on consent basis in both the states Maharashtra and Gujarat to reduce involuntary displacement. Consent camps are regularly organized to create awareness on the entitlement matrix & get final consent of the PAPs .

Out of 1434.47 hectares (As per RAP) of total land requirement, 1022.59 hectares (As per RAP) is private land. Till March 31<sup>st</sup> 2019, approximately 230.15 hectares of private land has been acquired through consent/direct purchase and in total (*comprising of Forest, Railways, Government and Private land*) 478.77 hectares of land has been acquired/transferred.

*Details Provided in Row 6 of Attachment M*

7. **Income Restoration Programme (IRP) Assistance:** RAP implementation agency have started to undertake “Training Need Assessment” surveys for identification of PAPs interested to undertake livelihood training. The priority district to start this activity were Ahmedabad, Anand and Kheda. The trade of training/training plan will be prepared after completion of training needs assessment survey. A draft Income Restoration Plan for Anand district have also been submitted to NHRCL by RAP implementation Agency.
8. **Relocation of Common Property Resources:** As on 31<sup>st</sup> March’ 2019 about 113 CPRs have been identified in the villages wherein JMS/JMR has been completed/submitted. Currently, NHRCL is in discussion with communities and land acquisition officers for relocation of common property resources.
9. **Grievance Redress:** NHRCL has submitted the proposal twice to establish grievance redressal committee to the state administration. Till the time district administration takes a decision on this proposal, NHRCL is resolving the grievances internally at the level of headquarter and Site offices through Land Acquisition Officers of District Administration. The record of grievances is maintained and also resolved. NHRCL is perusing with state and UT administration to expedite the process for establishing District Level Grievance Redressal Mechanism.

Since, RFCT-LARR 2013 has a provision of hearing grievances and objections by Collector/LAO’s at district level and all concern Collector/LAO’s are also resolving objections under Section-15 of the RFCT-LARR 2013. Thus, the State and District Administration may follow the same route without nomination of their representatives separately for District Level GRC.

However, NHRCL is in the process of establishing Level 1 (i.e. District Level Committee) with NHRCL nominated officials, Level 2 (i.e. Regional Level Committee) and Level 3 (i.e. Head Office Level Committee) Grievance Redressal Committee. NHRCL will notify/ upload all GRC details in public domain (i.e. NHRCL Website) by end of April’ 2019.

#### **Level 1: District Level Committee:**

- Dy. CPM (Chairman)
- Manager/Asst. Manager/Finance (DGM/AGM if no Manager/Asst. Manager are posted)
- Assistant Social Development Officer
- When District Administration nominate their officer, they shall automatically become part of District Level GRC.

#### **Level 2: Regional Level Committee**

- CPM (Chairman)
- GM/Contracts
- DGM/AGM/Finance
- Asst. Social Development Officer

#### **Level 3: Head Office Level Committee**

- Director/Projects, NHRCL (Chairman)
- Officer on Special Duty, NHRCL (Member)
- General Manager/Corp. Finance, NHRCL (Member)
- Chief Project Manager, NHRCL (Member)
- Social Development Officer, NHRCL (Secretary)

## *Annexure M*



2<sup>nd</sup> Quarter from January - March 2019

1 Progress of Land Acquisition and Resettlement											
Resettlement Activities	Unit	Planned Total	Progress in Quantity			Progress in %		Expected Date of Completion	Remarks	Implementing Party	
			During the Quarter	Till the Last Quarter	Up to the Quarter (Total Progress)	Till the Last Quarter	Up to the Quarter (Total Progress)				
1 Recruitment, training and deployment	1	Person-month	15X6=120	334X3=1002	64X3=192	1194	160	1045	Complete/ In-progress	1. Total Planned = As per page 149 in RAP institutional arrangement 2. During the quarter progress = 64 Details of Manpower deployed for Land Acquisition and Social work NHSRCL/HO - 7 Field Units - 327 3. To expedite the land acquisition process additional manpower has been deployed in DILR/LAO Office.	NHSRCL
	2	Person-month	180	79X3=237	92X3=276	513	153	285	Complete/ In-progress	1.Total Planned = 180 person month as per RAP implementation agency contract document. 2. No NGO has been hired for implementation. However it is planned in next quarter for income restoration program. In total 79 manpower is engaged in RAP Implementation Agencies and it is likely to increase next month onwards. 3. No. of CRs engaged by Arcadis = 52 (Details listed below) Maharashtra - 26 Gujarat & DNH. - 26 4.Additional resources of 27 manpower were added to expedite land acquisition process by engaging IEC (Information Education and Communication) agency like CPMA & RANE.	NHSRCL
	3	Number of NGO	5	0	0	0	0.00	0.00	In-progress	NGO will be engaged CPM wise. Thus, it is planned to engage five NGOs to cover 12 district and 1 Union Territory. Further, no. of NGO may also increase as per suggestion of RAP implementation agency in District wise IRP (Income Restoration Plan).	NHSRCL
	4	Number of Agency	1	1	0	1	0.00	100.00	Complete	Monitoring and Evaluation Agency LOI issued on 18.12. 2018. Team Mobilization from 10.01.2019.	NHSRCL
2 Progress of Joint Measurement Survey	1	Village	297	9	237	246	79.80	82.83	In-progress		NHSRCL
	2	Km	481.97	26.3	375.5	401.8	77.91	83.36	In-progress		NHSRCL
	3	Km	481.97	11.2	390.62	401.79	81.05	83.36	In-progress		NHSRCL
	4	Village	297	8	237	245	79.80	82.49	In-progress		NHSRCL
	5	Village	297	65	171	236	57.58	79.46	In-progress		NHSRCL
3 Valuation of Structures/Trees/Utilities	1	No. of Structures	3892	1096	1251	2347	32.14	60.30	In-progress	Planned Total = 3892 (As per RAP Pg. 15). JMS work is still in progress, thus the total scope can not be determined. Thus, planned total is taken from RAP.	NHSRCL
	2	No. of Structures	3892	938	681	1619	17.50	41.60	In-progress		NHSRCL
	3	No. of Structures	3892	938	944	1882	24.25	48.36	In-progress		NHSRCL
	4	No. of Trees	25270	5096	1429	6525	5.65	25.82	In-progress	Planned Total = 25270 (As per RAP Pg. 18). JMS work is still in progress, thus the total scope can not be determined. Thus, scope is taken from RAP.	NHSRCL
	5	No. of Trees	25270	5096	151	5247	0.60	20.76	In-progress		NHSRCL
	6	No. of Trees	25270	5096	1426	6522	5.64	25.81	In-progress		NHSRCL
	7	No. of Utilities	169	25	5	30	2.96	17.75	In-progress	1.Planned Total = 169 (As per RAP Pg. 16). JMS work is still in progress, thus the total scope can not be determined. Thus, scope is taken from RAP.	NHSRCL
	8	No. of Utilities	169	8	5	13	2.96	7.69	In-progress	2. Borewell, Toilet, Water Tank, Tube Well, Well, Handpump are considered as Utility.	NHSRCL
	9	No. of Utilities	169	4	5	9	2.96	5.33	In-progress		NHSRCL
4 Verification of Impacts after completion of JMS	1	No. of village	297	59	171	230	57.58	77.44	In-progress		NHSRCL
	2	No. of PAHs	14884	1056	8186	9242	55.00	62.09	In-progress	No. of PAH has been identified based on JMR Report.	NHSRCL
	3	No. of PAPs	68048	4576	37426	42002	55.00	61.72	In-progress		NHSRCL
	4	No. of PAHs	1887	1284	105	1389	5.56	73.61	In-progress	Planned Total = As per RAP No. of PAP's Displaced has been identified. However, consent survey is in-progress wherein PAH choice for relocation is to be determined i.e. PAH willing for Self Relocation or demanding project based relocation.	NHSRCL
	5	No. of PAPs	14884	97	540	637	3.63	4.28	In-progress	1. No. of PAPs identified for training in Ahmedabad, Kheda and Anand District. 2. For rest of the district identification is in-progress.	NHSRCL
5 Adopting the RAP	1	No. of reports	2	0	2	2	100.00	100.00	In-progress	Planned Total = 2 (1 no. RAP Summary in Gujarati & 1 no. RAP Summary in Marathi). The translated version are uploaded in NHSRCL website.	NHSRCL
	2	No. of campaign	297	20	145	165	48.82	55.56	In-progress		NHSRCL
6 Progress of Land Acquisition	1	Village	200	1	199	200	99.50	100.00	Complete	1. Section 11,16,19 & 21 is to be published for villages in Gujarat & DNH	NHSRCL
	2	Village	297	0	0	0	0.00	0.00		2. Draft Micro Plan has been prepared for villages wherein JMR has been approved by LAOs. However, it is under review by NHSRCL.	NHSRCL
	3	Village	200	78	84	162	42.00	81.00	In-progress		NHSRCL
	4	Village	200	98	44	142	22.00	71.00	In-progress		NHSRCL
	5	Village	200	0	0	0	0.00	0.00			NHSRCL
	6	Village	97	2	95	97	97.94	100.00	Complete	Namuna 1 & 3 is to be published for Maharashtra	NHSRCL
	7	Village	97	10	36	46	37.11	47.42	In-progress		NHSRCL
	8	No. of Plots	6963	1339	314	1653	4.51	23.74	In-progress	Planned Total = 6963 (Pvt. Plots). NHSRCL is signing Plot wise Consent in Gujarat and purchasing land through Direct Purchase in Maharashtra. Thus, the unit of planned total is been changed to no. of Plots. Till 31.03.19 consent/sale deed has been signed for 1653 private plots (230.15 Ha.). Further, 80% of the land compensation has also been disbursed and remaining 20% will be disbursed on final possession (for private plots only). Further, as on 31.03.19, in total (comprising of Forest, Railways, Government and Private land) 478.77 hectares land (in 2662 plots) have been acquired.	NHSRCL
9	Km	485.92	0	0	0	0.00	0.00	Not Applicable for this quarter	Contractor not mobilized yet	NHSRCL	
7 Income Restoration Programme (IRP) Assistance	1	No. of PAPs	14884	97	540	637	3.63	4.28	In-progress	PAPs identified for training in Anand & Kheda Districts	NHSRCL
	2	No. of Training Agency							In-progress	Identification of training agencies is under progress.	NHSRCL
	3	No. of persons	14884				0.00	0.00			NHSRCL
	4	No. of persons	14884				0.00	0.00			NHSRCL
	5	No. of Enterprises									NHSRCL
8 Relocation of Common Property Resources	1	No. of CPR	37	93	20	113	54.05	305.41	In-progress	Planned Total = 37 (As per RAP)	NHSRCL
	2	No. of CPR	37	0	0	0	0.00	0.00			NHSRCL
9 Grievance Redress	1	No. of GRCs	12	1	0	1	0.00	8.33	In-progress	NHSRCL is in the process of establishing Level 1 (i.e. District Level Committee) with NHSRCL nominated officials, Level 2 (i.e. Regional Level Committee) and Level 3 (i.e. Head Office Level Committee) Grievance Redressal Committee. NHSRCL will notify upload all GRC details in public domain (i.e. NHSRCL Website) by end of April 2019.	NHSRCL
	2	No. of cases	29	3	26	29	89.66	100.00	In-progress	Grievances have been drastically reduced due to signing of consent agreement /direct purchase of land.	NHSRCL
	3	No. of cases	29	3	26	29	89.66	100.00	In-progress	Field Verification is in-progress for un-resolved Grievance	NHSRCL
10 Develoment of Resettlement sites	1	No. of sites	30	0	0	0	0.00	0.00		Planned Total = 30 sites identified as per RAP	NHSRCL
	2	No. of PAHs	1887	0	0	0	0.00	0.00		Planned Total is as per RAP	NHSRCL
	3									Not applicable in this quarter	NHSRCL
	4	No. of relocation sites								Relocation Sites are being developed in consultation with District Administration.	NHSRCL
	5	No. of PAHs	1887	0	0	0	0.00	0.00		At present No. of PAHs Displaced has been identified, their verification and document collection is in-process. Further, also the consent survey is in-progress wherein PAH choice for relocation is to be determined i.e. PAH willing for Self Relocation or project assisted relocation. As of now it has been observed that majority of PAH are willing to take cash compensation for self-relocation.	NHSRCL
11 Performance Reporting	1	No. of Reports	3	3	0	3	0.00	100.00	Complete		RAP Implementation Agency (M/s)
	2	No. of Reports	0	0	0				In-progress	M&E Consultant mobilized from Jan.'2019 onwards.	RAP M&E Agency (M/s CRADLE)
	3	No. of Reports	1				0.00	0.00			RAP Implementation Agency (M/s)
	4	No. of Reports	3	1	1	2	33.33	66.67	In-progress		NHSRCL

2 Implementation of income restoration Assistance											
NHSRCL will monitor the change of living standard of the PAPs before and after the resettlement. When the PAPs are found that their living standard worsen, or whose present means of livelihood become non-viable, NHSRCL, in coordination with other appropriate institutions, will provide additional assistance.											
Brief Description of the implemented Income Restoration Program			Results during Report Period (No. of trainings implemented, No. of Participants, Etc)						Remarks		Location
									Not applicable in this quarter		

3 Restoration of income and living Standard								
Date of Survey								
No	Description about Surveyed Area	No. of Suveyed HHs	No. of PAHs with Increased incomes	No. of PAHs with Decreased incomes	No of PAHs with Unchanged incomes	Types of Problems Encountered	Solution provided	Perceived Need for Additional Assistance
1								
2								
4 Details of Stakeholder Meetings								
No	Date	Village/Tehsil/ District (no. of Participants)	Contents of the Consultation		Comments from Participants		Correspondences	
Gujarat								
1	02/01/19	Vaktana/Chorasi/Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
2	07/01/19	Kachodi/Chorasi/surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
3	10/01/19	Mohani/Chorasi/Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
4	11/01/19	Tham/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
5	12/01/19	Kholvad/Kamrej/Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
6	15/01/19	Pasodara/Kamrej/Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
7	16/01/19	Khadsad/Kamrej/Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
8	17/01/19	Telod/Amod/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
9	18/01/19	Panoli/Ankaleshwar/Bharuch and Untiyadra/Ankaleshwar/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
10	19/01/19	Tham/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
11	21/01/19	Uchand/Amod/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
12	22/01/19	Kosmada/Kamrej/Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
13	25/01/19	Sarfuddin/ Ankleshwar/ Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
14	28/01/19	Kanthariya/Tham/ Bharuch and Kholvad/ Kamrej/ Surat	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
15	29/01/19	Dehgam/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
16	30/01/19	Tralsa/Bharuch	Village level consultation meetings were held to discusson the Entitlement matrix and MAHSR project details.		PAPs enquired about benefits to be provided		As reported by RAP Consultant	
17	10/02/19	Vaghasi/Anand	Consultations were held with regard to identification of perspective PAPs for skill development training, need based assesement and further carrying out training demand assessment/survey.		All PAPS ready for filling up the training form		As reported by RAP Consultant	
18	16/02/19	Mogar/Anand	Consultations were held with regard to identification of perspective PAPs for skill development training, need based assesement and further carrying out training demand assessment/survey.		All PAPS ready for filling up the training form		As reported by RAP Consultant	
19	18/02/19	Vaghasi/Anand	Consultations were held with regard to identification of perspective PAPs for skill development training, need based assesement and further carrying out training demand assessment/survey.		All PAPS ready for filling up the training form		As reported by RAP Consultant	
20	19/02/19	Mogar/Anand	Consultations were held with regard to identification of perspective PAPs for skill development training, need based assesement and further carrying out training demand assessment/survey.		All PAPS ready for filling up the training form		As reported by RAP Consultant	
5 Details of Grievance Redress								
No	Date of Receipts of Complaints	Contents of the Complaints			Action taken by NHRCL		Resolved / Not Yet Resolved	
1	07/01/19	The representation regarding ownership dispute			The matter was resolved with concern district authority.		Resolved	
2	05/03/19	Objection pertaining to acquisition of land			NHRCL informed the party about the mitigation measure adopted to reduce the project impact.		Resolved	
3	13/03/19	Request for not acquision of school's limited activity ground, library room and stage			Technical design were studied and appropriate actions were taken to reduce the impact on the structure.		Resolved	
