

QUARTERLY PROGRESS REPORT – III (APRIL – JUNE 2019)

RAP Implementation Monitoring Format (Annexure M)

for

Mumbai – Ahmedabad High Speed Rail Limited

Submitted by:

NATIONAL HIGH SPEED RAIL CORPORATIONLIMITED 2nd FLOOR, ASIA BHAWAN, ROAD NO-205, DWARKA SECTOR 9, NEW DELHI – 110077

Quarterly Progress Report Number 3


Time-Frame: 1st April' - 30 th June, 2019

PROJECT AT GLANCE

The Ministry of Railways formulated the Indian Railways Vision 2020 in December 2009. The vision aims to modernize the existing conventional lines and enhance their traffic capacity as well as develop high-speed railway lines. Seven routes were selected as candidates for the high-speed railway system. Among them, the Mumbai—Ahmedabad route was given top priority by the Experts Committee on Modernization of India's National Railways established by the Ministry of Railways. Based on this plan, the Mumbai—Ahmedabad High-Speed Railway will be implemented. In this context, Japan and India issued a joint statement in May 2013 committing to conduct a joint study on the Project. Based on this decision, the Joint Feasibility Study for Mumbai-Ahmedabad High-Speed Railway Corridor was conducted from December 2013 to June 2015. Then, the Prime Ministers of Japan and India issued a joint statement in December 2015, agreeing to introduce the Shinkansen High-Speed Railway (HSR) System to the Mumbai Ahmedabad route

Figure 1: Route of Mumbai-Ahmedabad High-Speed Railway line

The Mumbai-Ahmedabad High-Speed Railway Line (HSRL) will connect Mumbai, the capital city of Maharashtra and the second most populous metropolitan area in India, with Ahmedabad which is a metropolis in Gujarat. The approximately 508-km-long line will consist of high-speed railway running along the Arabian Sea coast and connecting with Surat and Vadodara en route which are the second and third largest city in Gujarat. The alignment will pass through Maharashtra,

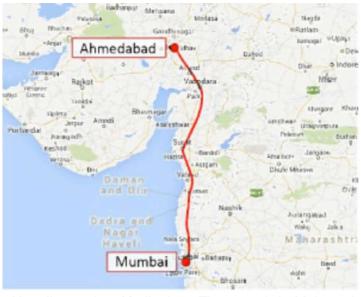

Gujarat and part in Dadra & Nagar Haveli covering 12 districts. The stretch in Maharashtra is 155.72 km, the stretch in Dadra & Nagar Haveli is 4.3 km and stretch in Gujarat is 348.15 km.

1. TOTAL LAND REQUIREMENT FOR THE PROJECT

In total, 7359 land plots with area comprising 1379.62 ha of land in 297 villages is required for the project. This includes private land, government land, forest land and land of Indian Railways. Around 72.40% of land plots affected are private land and remaining land belongs to Indian Railways, Government land and forest land.

2. KEY OBJECTIVE OF RESETTLEMENT ACTION PLAN

The main objective of the detailed resettlement action plan (RAP) is to ensure that the project design and implementation are socially acceptable based on the JICA Guidelines for Environmental and Social Considerations, 2010¹. From July, 2017 to July 2018, a Social Impact Assessment Study was done based on which a RAP has been prepared. The RAP is approved by NHSRCL as per no. NHSRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/2588 dated 12.09.2018. It has identified all potential social issues in the project and has developed mitigating measures for the impact of the project. The total estimated cost of implementing the RAP is ₹16,729.85 crores.

3. PROJECT IMPACT

The project being linear in nature is not expected to result in large-scale displacement of community. Impact on livelihood is mainly due to the acquisition of private agricultural land and business units along the project corridors. District-wise details of Project Impacts are presented in the table below.

SUMMARY OF PROJECT IMPACTS (As per RAP)

- > Total Number of Project Affected Household: 14,884
- Number of Affected Title Holder: 10,305
- Number of Affected Non-Title Holder: 4,579
- > Total Number of Affected Structures: 3892
- Total Number of Affected CPRs: 37
- Total Number of Affected Commercial Structures: 271
- > Total number of Impacted Trees: 37,394

4. Monitoring of Resettlement Action Plan

From July, 2017 to July 2018, a Social Impact Assessment Study was done based on which a RAP has been prepared. The RAP is approved by NHSRCL as per no. NHSRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/2588 dated 12.09.2018. It has identified all potential social issues in the project and has developed mitigating measures for the impact of the project.

NHSRCL is submitting the third quarterly progress report to JICA for the period of April 1^{st} , 2019 to June 31^{st} , 2019.

¹ https://www.jica.go.jp/english/our_work/social_environmental/guideline/pdf/guideline100326.pdf

KEY HIGHLIGHTS OF THIS QUARTER

- 1. <u>Engagement of Staff for RAP Implementation:</u> NHSRCL has engaged human resources to cover this aspect at all three levels- Headquarters, Districts and Villages.
 - **a.** NHSRCL's senior management along with Social Development Officer and Assistant Social Development Officer is in charge of matters at Headquarter level.

i.	Managing Director	- 1
ii.	Director (Projects)	- 1
iii.	Officer on Special Duty	- 1
iv.	Social Development Officer	- 1
٧.	Assistant Social Development Officer	- 1
۷İ.	Project Managers (Civil)	- 1
vii.	Project Managers (QAQC)	- 1

b. At the site 5 Chief Project Managers at Ahmedabad, Vadodara, Surat, Palghar and Mumbai are managing land acquisition and Resettlement Action Plan implementation related issues in Gujarat, Dadar & Nagar Haveli and Maharashtra. The details of staff deployed is given below.

S.	District	NHSRCL			
No.		DILR/LAO's Office	Communicators	NHSRCL's Staff	
		Office		Permanent	Temporary/ Out-sourced Staff/Revenue
1	MUMBAI SUBURBAN	0	0	0	0
2	THANE	11	10	3	13
3	PALGHAR	16	0	11	45
4	DNH	0	0	0	1
5	VALSAD	5	17	5	10
6	NAVSARI	6	0	0	0
7	SURAT	8	8	2	5
8	BHARUCH	7	13	3	4
9	VADODARA	25	15	3	9
10	ANAND	7	4	1	4
11	KHEDA	8	8	1	9
12	AHMEDABAD	6	4	3	6
	Total	99	79	32	106

c. Through RAP implementing agency i.e. M/s Arcadis about 79 manpower has been deployed for land acquisition and social safeguard activities. Further, additional deployment of about 54 manpower has also been done by engaging two agencies i.e. CPMA and RANE for Information Education and Communication activities in Palghar district.

Details Provided in Row 1 of Attachment M

2. Progress of Joint Measurement Survey: Out of total 297 villages falling in the project alignment, field-work for JMS has been completed in 251 villages. This is around 85 percent of the total villages. The other steps involved include preparation of Joint Measurement Reports for the villages, submission to district authorities and subsequent approval. Approximately 81% of the Joint Measurement Reports submitted to district administration have been approved by Land Acquisition Officer. Efforts are in place to expedite the process to complete the remaining stretch of JMS.

Details Provided in Row 2 of Attachment M.

3. Valuation of Properties attached to the structure:

Valuation has to be done for structures, tress and utilities attached to the land being acquired. After confirmation on numbers in Joint Measurement Report, the values of the structure is calculated by government authorized valuer. The details are further confirmed by Road & Building Department in Gujarat and Public Works Department in Maharashtra and DNH.

Details Provided in Row 3 of Attachment M

4. Verification of Impacts after completion of JMS

NHSRCL created a software for Management Information System in March, 2019. After Joint Measurement Reports for the villages are finalized by the district administration, the complete details are filled in the software. While 14884 households were identified at the time of socioeconomic survey during RAP, for the villages where JMS have been completed & JMR are received, the number of Project Affected Households are 9470 and corresponding number of project affected persons identified are 42944.

Details Provided in Row 4 of Attachment M

5. Adopting the RAP

RAP has been summarized and translated into Gujarati and Marathi and the same has also been uploaded in NHSRCL Website. NHSRCL has also submitted a copy to all land acquisition officers. Further, communication campaigns are also been organized for Project Affected Persons (PAP).

Details Provided in Row 5 of Attachment M

6. Progress of Land Acquisition

At present, NHSRCL is acquiring land on consent basis in both the states Maharashtra and Gujarat to reduce involuntary displacement. Consent camps are regularly organized to create awareness on the entitlement matrix & get final consent of the PAPs .

As per RAP, the total land requirement was 1434.47 hectares, however at present, total land requirement is reduced to 1,379.62 ha (154.66 ha governmental land, 127.50 ha railways land, 998.78 ha private land, 98.68 ha forest land). Till June 30th 2019, approximately 306.54 hectares of private land has been acquired through consent/direct purchase and in total (comprising of Forest, Railways, Government and Private land) 555.16 hectares of land has been acquired/transferred.

Details Provided in Row 6 of Attachment M

7. <u>Income Restoration Programme (IRP) Assistance:</u> RAP implementation agency have started to undertake "Training Need Assessment" surveys for identification of PAPs interested to undertake livelihood training. The priority district to start this activity were Ahmedabad, Anand and Kheda. The trade of training/training plan will be prepared after

completion of training needs assessment survey. A draft Income Restoration Plan for Anand district have also been submitted to NHSRCL by RAP implementation Agency.

- **8.** Relocation of Common Property Resources: As on 30th June' 2019 about 113 CPRs have been identified in the villages wherein JMS/JMR has been completed/submitted. During JMS ROW marking has been done on ground, based on the field survey new affected additional CPRs has been identified. Currently, NHSRCL is in discussion with communities and land acquisition officers for relocation of common property resources.
- 9. <u>Grievance Redress:</u> The RFCT-LARR 2013 has a mechanism of hearing grievances and objections by Collector/LAO's at district level and all concern Collector/LAO's are also resolving objections under Section-15 of the RFCT-LARR 2013. Thus, the State and District Administration may follow the same route without nomination of their representatives separately for District Level GRC.

However, NHSRCL has established Level 1 (i.e. District Level Committee), Level 2 (i.e. Regional Level Committee) and Level 3 (i.e. Head Office Level Committee) Grievance Redressal Committee. NHSRCL has also notified/uploaded all GRC details in public domain (i.e. NHSRCL Website).

10. <u>Details on Consent Camp</u>: During the quarter 233 no. of consent camp has been held and 181 no. of stakeholder and village level consultations has been held by RAP Implementation Agency.

Annexure M

1 Progress of Land Acquisition and Resettlement Resettlement Activities Unit Planned Total Remarks Up to the Quarter (Total Progress) During the Quarte Progress) Total Planned = As per page 149 in RAP institu During the quarter progress = 64 Details of Manpowe eployed for Land Acquisition and Social work
HSRCLHO - 7
leld Units - 449 tting up SEMU and placement of staff erson-month 15X8=120 456X3=1368 1194 2562 1045 2135 HSRCL progress Total Planned = 180 person month as per RAP impleme . No NGO has been hired for implementation. However Recruitment, training and deployment Deployment of RAP implementing human resource/ implementing NGOs by Arcadis at the site 417 180 79X3=237 513 750 285 .Additional resources of manpower were added to expedite 4. Additional resources of manpower were added to expedite land acquisition process by engaging IEC (Information Education and Communication) agency like CPMA & RANE. NGO will be engaged CPM west. Thus, it is planned to engage five NGOs to cover 12 district and 1 Union Territory, Further, no of NGO may also increase as per suggestion of RAP implementation agency in District wise IRP (Income Restoration) eployment of specialist/local NGOs for preparing and iplementing Income Restoration Plan umber of NGO 0.00 20.00 In-progress nitoring and Evaluation Agency LOI issued on 18.12. 2018 am Mobilization from 10.01.2019. Deployment of External Monitoring Agency (EMA) lumber of Agen 1 1 1 1 100.00 100.00 Complete IHSRCL mber of villages for which Field work of Joint Measurement rvey is complete n-progres otal length for which ROW Marking is completed 481.97 425.0 83.36 23.2 401.8 88.18 In-progress Progress of Joint Measurement Survey HSRCL 3 481.97 3.6 401.79 405.36 83.36 84.10 In-progres mber of JMS Reports verified by Department of Land 297 82.49 82.83 In-progress 5 umber of JMS reports approved by Land Acquistion Office 297 236 241 79.46 81.14 NHSRCL Planned Total = 3892 (As per RAP Pg. 15). JMS work is still in progress, thus the total scope can not be determined. Thus, planned total is taken from RAP. NHSRCL 3892 3883 2347 6230 60.30 160.07 lo. of Structures In-progress 2 Valuation approved by Concerned Dept. (PWD/R&B etc.) No. of Structure 3892 2281 1882 4163 48.36 106.96 About 6230 no of structures have been identified in the villages wherein JMS/JMR has been completed/submitted. During JMS 760W marking has been done on ground, based on the field survey new affected additional structures has been identified.

Planned Total = 25270 (As per RAP Pg. 18) JMS work is still invorgerss, thus the total scope can not be determined. Thus, scope is taken from RAP. /aluation approved by Land Acqusition Officer 3 lo. of Structures 3892 1121 1619 2740 41.60 70.40 In-progress . of Trees 25270 19092 25.82 75.55 In-progress Valuation of Structures/Trees/Utilitie 'aluation approved by Concerned Dept. (PWD/R&B etc.) lo. of Trees 25270 10543 6522 17065 25.81 67.53 uation approved by Land Acqusition Officer No. of Trees 25270 10543 5247 15790 20.76 62.49 6 In-progress /aluation completed 7 lo. of Utilities 169 45 30 17.75 44.38 75 .Planned Total = 169 (As per RAP Pg. 16). JMS work is still in rogress, thus the total scope can not be determined. Thus, cope is taken from RAP. Borewell,Toilet,Water Tank,Tube Well,Well,Handpump are Valuation approved by Concerned Dept. 8 No. of Utilities 169 45 13 58 7.69 34.32 In-progress 169 24 9 Filling of data into NHSRCL's internal management informat o. of village 77.44 297 15 230 245 82.49 In-progress lo. of PAH has been identified based on JMR Report. 2 Number of project affected household identified lo. of PAHs 14884 228 9242 9470 62.09 63.63 NHSRCL Number of project affected people identified No. of PAPs 68048 942 42002 42944 61.72 63.11 In-progress Planned Total = As per RAP to, of PAP's Displaced has been identified. However, consen-survey is in-progress whrein PAH choice for relocation is to be tetermined i.e. PAH willing for Self Relocation or demanding reject based relocation. NHSRCL Verification of Impacts after completion of JMS imber of people identified for relocation lo. of PAHs 1887 65 1389 1454 73.61 77.05 In-progress No. of PAPs identified for training in Anand, Kheda, Vac 5 entification of PAPs for training o. of PAPs 14884 97 734 4.28 637 4.93 ISRCL In-progress anned Total = 2 (1 no. RAP Summary in Gujarati & 1 no. RAF ummary in Marathi). The translated version are uploaded in HSRCL website. anslation of RAP report into local language lo. of reports 2 2 2 2 100.00 100.00 In-progres Adopting the RAP mmunication campaign are regularly organised. At times on-age is been visited multiple times as consent is also in anization of communication campaign for RAP awareness ln. of campaig 297 181 165 346 55.56 116.50 Section 11,16,19 & 21 is to be published for villages ujarat & DNH Publication of Section 11 Notification 200 200 200 100.00 100.00 Complete Definition of the Court of the 2 lization of Micro-Plan 297 0.00 0.00 illage 0 0 0 NHSRCI Publication of Section 16 Notification(Preparation of details) 200 162 170 81.00 85.00 illage In-progress ISRCL 4 Publication of Section 19 notification illage 200 27 142 169 71.00 84.50 In-progress HSRCL 200 126 126 0.00 63.00 llage amuna 1 & 3 is to be published for Maharashtra ublication of Namuna 1 Notification in Maharashtra 97 97 97 100.00 100.00 Complete blication of Namuna 3 Notification in Maharashtra 97 47.42 47.42 /illage 46 46 In-progress 0 Planned Total = 7359 (Pvt. Plots Based on updated survey no./area as per latest revenue records/village maps where JMR (Joint Measurement Report) approved; NHSRCL is signing Plot wise Consent in Gujarat and purchasing land through Direct Purchase in Maharashtra. Thus, the unit of planned total is been changed to no. of Plots. Progress of Land Acquistion bursement of Land Compensation and R&R Assistance No. of Plots 7359 701 1653 2354 23.74 31.99 NHSRCL compensation has also been disbused and remaing 20% will be disbursed on final possession (for private plots only). Further, as on 30.06.19, in total (comprising of Forest, Railways, Government and Private land) 555.16 hectares land (in 3263 plots) have been acquired out of total 1379.62 Ha. (in 8925 plots), identified as per JMR. Not Applicable fo this quarte 0 HSRCL andover Encumberence free land to Contractor 485.92 0 0 0.00 0.00 nber of Project Affected persons eligible/ identified for Ps identified for training in Gujarat & Mahan No. of PAPs 14884 97 637 734 4.28 4.93 NHSRCL dentification of training agencies is under progress. No. of Training mber of training agencies identified HSRCL 2 0.00 20.00 In-progress Income Restoration Programme (IRP) Assistance o. of persons 14884 28 28 0.00 0.19 of persons 14884 0.00 0.00 . of Enterprise entification of CPRs to be relocated lo of CPR 37 113 113 305.41 305.41 mber of CPRs reloacted o. of CPR 0.00 0.00 2 37 0 0 0 NHSRCL has established Level 1 (i.e. District Level Committee) with NHSRCL nominated officials, Level 2 (i.e. Regional Level Committee) and Level 3 (i.e. Head Office Level Committee) Grievance Redressal Committee. NHSRCL has also notified/uploaded all GRC details in public domain (i.e. NHSRCL Webste) stablishment of Grievance Regress Communi GRCs)/Public complaint resolving Meetings ievance Redress rievances have been drastically reduced due to signing or ensent agreement /direct purchase of land. 2 eiving complaints / claims form PAPs No of cases 34 29 34 100.00 100.00 IHSRCL In-progress No of cases 34 29 34 100.00 esponded complaints / claims 100.00 In-progres Palnned Total = 30 sites identified as per RAP 1 30 0.0 0.00 0.00 NHSRCL No. of sites 0 0 imber of Project Affected Households shifted to temporary nned Total is as per RAP No. of PAHs 1887 0.00 0.00 0.0 o-ordination with different depatments to provide basic menties at proposed locations elocation Sites are being developed in consultation with istrict Administration. No. of relocation umber of relocation/resettlement sites developed esettlement sites t present No. of PAH's Displaced has been identified, erification and document collection is in-process. Further, also the consent survey is in-progress whrein PAH choice for relocation is to be determined i.e. PAH willing for Self Relocation or project assisted relocation. As of now it has been observed that majority of PAH are willing to take cash compensation for self-relocation. Number of Project Affected Household relocated No. of PAHs 1887 0 0 0.00 0.00 NHSRCL fonthly Progress Report (submitted by Arcadis to NHSRCL) No. of Reports 3 3 3 3 100.00 100.00 Complete Quarterly progress report (submitted by M&E Consultant to NHSRCL) M&E Consultant mobilzed from Jan.'2019 onwards. 2 1 1 0 1 No. of Reports In-progress nal Report (submitted by Arcadis to NHSRCL) HSRCL 4 Submission of Quarterly progress report from NHSRCL to JICA No. of Reports 2 3 66.67 100.00 In-progress 2 Implementation of income restoration Assistance
NHSRCL will monitor the change of living standard of the PAPs before and after the resettlement. When the PAPs are found that their living standard worsen, or whose present meant of livelihood become non-viable, NHSRCL, in coordination with other appropriate institutions, will provide additional assistances. Brief Description of the implemented Income Restoration Program Results during Report Period (No. of trainings implemented, No. of Participants, Etc) Remarks Location 28 candidates are undergoing t

3 Restoration of	income and living Standard							
Date of Survey No Description about Surve		No. of PAHs with Increased incomes	No. of PAHs with	No of PAHs with	Types of	Solution provided		Perceived Need for Additional Assistance
Area			Decreased incomes	Unchanged incomes	Problems Encountered			
1 2								
	ceholder Meetings Village/Tehsil/ District (no. of Participants)	Contents of the Consultation	•	Comments from	Participants	•	Corresponde	nces
1 1 April, 2019	Rayka/Vadodara/Vadodara	Land Compensation				tisfied with the		onsultants
2 1 April, 2019 3 1 April, 2019	Kathor & Kholvadi/Kamrej/Surat Dungral/vapii/Valsad	Rate Of Land Resettlement & Rehabilita	ation Package	informatio	n provide	d by NHSRCL & eeded for consent		
4 1 April, 2019 5 2 April, 2019 6 2 April, 2019	KochvalVapi/Valsad Rayka & DodkalVadodaralVadodara Ravidra/Rokleshwar/Bharuch	Entitlement Matrix	_	agreemer	nt			
7 2 April, 2019 8 2 April, 2019	Kathor & Kholvad/Kamrej/Surat Kochrva/Vapi/Valsad	Skill Development Trainir Procedure for Consent A		declared b		Gujarat the rate ere accepted by		
9 2 April, 2019 10 2 April, 2019 11 3 April, 2019	Dungra/Vapi/Valsad Pathri/ValsadValsad Mahudhala/Bharuch/Bharuch	_				the training prog.		
12 3 April, 2019 13 3 April, 2019 14 3 April, 2019	Oviyan/Kamrej/Surat Karvad/Vejn/Alsad Dungra/Vejn/Alsad			Of NHSR(about the		ey also enquired training.		
15 4 April, 2019 16 4 April, 2019	Oung avapivasau Dung avapivalsau PalanValsadValsad PalanValsadValsad	_ _ _						
17 4 April, 2019 18 5 April, 2019 19 5 April, 2019	Dungra/Vapi/Valsad Oviyan/Kamrej/Surat Daswara/Pardi/Valsad							
20 6 April, 2019 21 6 April, 2019	Ajod/Vadodara/Vadodara Kachholi & Bhatia/Kamrej/Surat							
22 6 April, 2019 23 8 April, 2019 24 9 April, 2019	Sonwada/Valsad/Valsad Dashrath/Vadodara/Vadodara Kosmada/Kamrej/Surat							
25 9 April, 2019 26 10 April, 2019	Kochrva/Vapi/Valsad Borigram/Umbergaon/Valsad							
27 11 April, 2019 28 11 April, 2019	Chapad/Vadodara/Vadodara Laskana/Kamrej/Surat							
29 11 April, 2019 30 12 April, 2019	Ramnagar/Anand/Anand Borigram/Umbergaon/Valsad							
31 13 April, 2019 32 15 April, 2019	Ajod/Vadodara/Vadodara Mogar/Anand/Anand Varbara Mogi Motional							
33 15 April, 2019 34 17 April, 2019 35 18 April, 2019	Kochrva/Vapi/Valsad Antroli & Niyol/Palsana/Surat Umarwada/Ankleshwar/Bharuch	‡						
35 18 April, 2019 36 18 April, 2019 37 18 April, 2019	Omarwadazenkiesi warishia don Antoili/BasanSurat Bhanji Faliya/Valsad/Valsad	1						
38 19 April, 2019 39 19 April, 2019	Handod/Vadodara/Vadodara Umarwada/Ankleshwar/Bharuch							
40 19 April, 2019 41 24 April, 2019	Bhanji Faliya/Valsad/Valsad Antrolii/Palsana/Surat	1						
42 24 April, 2019 43 25 April, 2019	Boriavi/Anand/Anand Umarwada/Ankleshwar/Bharuch Convant/Valsedt/Valsed	1						
44 25 April, 2019 45 26 April, 2019 46 26 April, 2019	Gorvada/Valsad/Valsad Antrolii/Palsana/Surat Gorvada/Valsad/Valsad	-						
46 26 April, 2019 47 27 April, 2019 48 27 April, 2019	Gurvadar valsaur valsaur DeshrathVadodrar al Vadodara Kambola/Karjan/Vadodara	-						
49 27 April, 2019 50 28 April, 2019	Tutanioraria par vedodara Jujiwa/Valsad/Valsad Chhani/Vadodara/Vadodara]						
51 29 April, 2019 52 29 April, 2019	Tralsi/Bharuch/Bharuch Bavra/Mehdabad/Kheda							
53 30 April, 2019 54 1 May, 2019	Endergota/Valsad/Valsad Kalipur/Karjan/Vadodara							
55 2 May, 2019 56 2 May, 2019	Manjalpur/Vadodara City/Vadodara Manpur/Karjan/Vadodara Manpur/Karjan/Vadodara							
57 3 May, 2019 58 3 May, 2019 59 3 May, 2019	Asarwa/Asarwa/Ahmedabad Maneja/Vadodara Cityl/Vadodara Kanji/Nadiad Rural Area/Kheda							
60 4 May, 2019 61 4 May, 2019	Adas/Anand Boriyavi/Anand							
62 4 May, 2019 63 4 May, 2019	Shihor/Karjan/Vadodara Bhatia/Chorasi/Surat	<u> </u>						
64 6 May, 2019 65 6 May, 2019	Sankarada/Vadodara/Vadodara Kachholi/Chorasi/Surat							
66 8 May, 2019 67 8 May, 2019	Padmala/Vadodara/Vadodara Dora/Amod/Bharuch							
68 8 May, 2019 69 8 May, 2019 70 9 May, 2019	Aloonj/Ankleshwar/Bharuch Pipaliyaa/Bharuch/Bharuch Pingalwada/Karjan/Vadodara	_						
71 9 May, 2019 72 10 May, 2019	Tralsa/Paruch/Bharuch Khanda/Karjan/Vadodara	-						
73 11 May, 2019 74 14 May, 2019	Dehgam/Nadiad Rural Area/Kheda Bodka/Karjan/Vadodara							
75 14 May, 2019 76 14 May, 2019	Vadsar/Vadodara City/Vadodara Piplag/Nadiad/Kheda							
77 14 May, 2019 78 16 May, 2019	Bhumel/Nadiad/Kheda Karela/Bharuch/Bharuch Chaklasi/Nadiad Rural Area/Kheda							
79 17 May, 2019 80 18 May, 2019 81 18 May, 2019	Chakasin/Nadiad Nufa Area/Neba Manjalpur/Vadodara City/Vadodara Uttarsanda/Nadiad Rural Area/Kheda	<u> </u>						
32 20 May, 2019 33 20 May, 2019	Bhumel/Nadiad Rural Area/Kheda Adas/Anand	_						
34 23 May, 2019 35 24 May, 2019	Maretha/Padra/Vadodara Uttarsanda/Nadiad Rural Area/Kheda							
36 27 May, 2019 37 27 May, 2019	Rayka/Vadodara/Vadodara Bodka/Vadodara/Vadodara							
38 27 May, 2019 39 27 May, 2019 30 27 May, 2019	Chapad/Vadodara/Vadodara Chhani/Vadodara/Vadodara Ajod/Vadodara/Vadodara	‡						
91 27 May, 2019 92 29 May, 2019	Adas/Anand Samarkha/Anand/Anand]						
29 May, 2019 30 May, 2019	Ghadoi/Valsad/Valsad Khajurdi/Valsad/Valsad							
95 4 June, 2019 96 4 June, 2019	Khanda/Karjan/Vadodara Thikriya Mubarak/Vadodara Rural/Vadodara Mangur Kirian/Vadodara	1						
97 5 June, 2019 98 11 June, 2019 99 11 June, 2019	Manpur/Karjan/Vadodara Tarsadi/Mangrol/Surat Jujwa/Valsad/Valsad	1						
11 June, 2019 11 June, 2019 11 June, 2019	uguwa vaisau vaisau Handodikarjan/Vadodara Padmalar/Vadodara Rural/Vadodara	1						
02 12 June, 2019 03 12 June, 2019	Dashrath/Vadodara Rural/Vadodara Bodkal/Karjan/Vadodara]						
04 12 June, 2019 05 13 June, 2019	Tham/Bharuch/Bharuch Vaghsi/Anand/Anand	1						
06 13 June, 2019 07 13 June, 2019	Dumral/Nadiad Rural Area, Mehdavad/Kheda Katekpura/Nadiad Rural Area, Mehdavad/Kheda Sukhlaw/Dart/Molead	_						
08 14 June, 2019 09 14 June, 2019 10 14 June, 2019	Sukhlav/Pardi/Valsad Velparva/Pardi/Valsad Maneja/Vadodara Citjy/Vadodara	-						
10 14 June, 2019 11 15 June, 2019 12 15 June, 2019	manejarvauousa urijyrvauousa VaghaldharAvlasad/Valsad KarodiyalVadodara City/Vadodara	1						
3 17 June, 2019 4 17 June, 2019	Tundel/Nadiad Rural Areal/Kheda Shakarda/Vadodara City/Vadodara							
15 17 June, 2019 16 18 June, 2019	Telod/Amod/Bharuch Antrol/Palsana/Surat	1						
17 18 June, 2019 18 18 June, 2019	Uttarsanda/Nadiad Rural Area/Kheda Pingalwada/Karjan/Vadodara Manajan/adodara Citi/Jadodara	1						
19 18 June, 2019 20 19 June, 2019 21 19 June, 2019	Maneja/Vadodara City/Vadodara Vaktana/Chorasi/Surat Antroil/Palsana/Surat	‡						
21 19 June, 2019 22 19 June, 2019 23 19 June, 2019	Antrour-assana:oura Virpur/Vadodara Rural/Vadodara Pipaliyaa@haruch@haruch	1						
24 20 June, 2019 25 20 June, 2019	Niyol/Palsana/Surat Shihor/Vadodara Rural/Vadodara]						
26 20 June, 2019 27 20 June, 2019	Aloonj/Ankleshwar/Bharuch Dehgam/Bharuch/Bharuch]						
28 21 June, 2019 29 21 June, 2019	Mangrol/Tarsadi/Surat Shihor/Vadodara Rural/Vadodara	1						
30 22 June, 2019 31 22 June, 2019	Kosmadal/kanrej/Surat Medhad/Vadotar Rural/Vadodara Deboam/Bharush Bharush	1						
32 24 June, 2019 33 25 June, 2019 34 25 June, 2019	Dehgam/Bharuch/Bharuch Oviyan/Kamrej/Surat Kukarwada/Bharuch/Bharuch	‡						
34 25 June, 2019 35 26 June, 2019 36 26 June, 2019	kukarwadarishar uchrenaruch Velparva/Pardi/Valsad Rajpur-Hirpur/Maninagar/Ahmedabad	1						
37 26 June, 2019 38 26 June, 2019	Kajpur i ini por ima ini ingar i mendudud. Chansad/yadodara Rural//adodara Tralsa/Bharuch/Bharuch	1						
39 26 June, 2019 40 27 June, 2019	Kukarwada/Bharuch/Bharuch Ambach/Pardi/Valsad							
41 27 June, 2019 42 27 June, 2019	Dehgam/Nadiad Rural Area/Kheda Chansad/Vadodara Rural/Vadodara	1						
43 29 June, 2019	Padariya/Bharuch/Bharuch	<u> </u>						

4	4 Details of Stakeholder Meetings								
No	Date	Village/Tehsil/ District (no. of Participants)	Contents of the Consultation	Comments from Participants	Correspondences				
MAI	IARASHTRA		Land Compensation	• PAPs who were satisfied with	RAP Consultants				
1	4 April, 2019	Bilalpada & More/Vasai/Palghar	-		1011 Constituits				
2	12 April, 2019	More/Vasai/Palghar	Rate Of Land	the information provided by					
4	15 April, 2019	Kharbav/Bhiwandi/Thane	Resettlement & Rehabilitation Package	NHSRCL					
5	16 April, 2019	Kharbav/Bhiwandi/Thane	Entitlement Matrix	 PAPs appreciated the training 					
6	17 April, 2019	Kharbav/Bhiwandi/Thane	Skill Development Training	prog. of NHSRCL and they also					
7	18 April, 2019	More/Vasai/Palghar	Procedure for Consent Agreement						
8	19 April, 2019	More/Vasai/Palghar	Procedure for Consent Agreement	enquired about the details of					
9	18 April, 2019	More/Vasai/Palghar	1	training.	!				
10	19 April, 2019	Kharbav/Bhiwandi/Thane	1						
1	19 April, 2019	Padle/Thane/Thane			!				
11	20 April, 2019	Padle/Thane/Thane							
12	20 April, 2019	Paye/Bhiwandi/Thane							
13	22 April, 2019	Kharbav/Bhiwandi/Thane							
14	22 April, 2019	Shil/Thane/Thane							
15	24 April, 2019	Desai/Thane/Thane							
16	25 April, 2019	Shil/Thane/Thane	1		!				
17	25 April, 2019	Desai/Thane/Thane							
18	26 April, 2019	Kharbav/Bhiwandi/Thane	1						
19	27 April, 2019	Gokhiware/Vasai/Palghar	1						
20	30 April, 2019	Kharbav/Bhiwandi/Thane							
39	1 May, 2019	More & Bilalpada/Vasai/Palghar							
40	2 May, 2019	More & Bilalpada/Vasai/Palghar							
41	2 May, 2019	Desai/Thane/Thane							
42	3 May, 2019	Desai/Thane/Thane							
43	4 May, 2019	Desai/Thane/Thane							
44	7 May, 2019	Bilalpada & More Goan/Vasai/Palghar							
45	9 May, 2019	Bhilalpada/Vasai/Palghar							
46	9 May, 2019	Manoli/Bhiwandi/Thane							
47	9 May, 2019	Gokhivare, Poman , Sarjamori , Shilottar/Vasai/Palghar							
48	10 May, 2019	Gokhivare, Poman , Sarjamori , Shilottar/Vasai/Palghar							
49	22 May, 2019	Desai/Thane/Thane							
50	24 May, 2019	Desai/Thane/Thane			!				
51	24 May, 2019	Padle & Desai/Thane/Thane							
52	28 May, 2019	Shil/Thane/Thane							
53	28 May, 2019	Bilalpada & More Goan/Vasai/Palghar							
54	30 May, 2019	Padle/Thane/Thane							
21	4 June, 2019	Shil/Thane/Thane	1						
22	6 June, 2019	Shil/Thane/Thane							
23	7 June, 2019	Shil/Thane/Thane							
24	10 June, 2019	Shil/Thane/Thane							
25	11 June, 2019	Desai/Thane/Thane	-						
26	12 June, 2019	Devale/Thane/Thane	-						
27	12 June, 2019	Desai/Thane/Thane	1						
28	13 June, 2019	Desai/Thane/Thane	1						
29	14 June, 2019	Kalher/Bhiwandi/Thane Desai/Thane/Thane	1						
30	17 June, 2019	Desai/Thane/Thane Desai/Thane/Thane	1						
31	19 June, 2019 20 June, 2019	Desai/Thane/Thane Desai/Thane/Thane	1						
33	20 June, 2019 21 June, 2019	Desai/Thane/Thane	1						
33	·	Kalher/Bhiwandi/Thane	1						
35	22 June, 2019	Betwade and Aagasan/Thane/Thane	1						
36	24 June, 2019 25 June, 2019	Betwade/Thane/Thane	1						
37	26 June, 2019	Padle/Thane/Thane	1						
38	29 June, 2019	Kalher/Bhiwandi/Thane							
50	20 00110, 2010		<u> </u>	1					

5 Details of Grievance Redress

No	Date of Receipts of Complaints	Contents of the Complaints	Action taken by NHSRCL	Resolved / Not Yet Resolved		
1	12.04.2019	Compensation for loss of dwelling unit in Society (Ahmedabad)	NHSRCL is in discussion with State Authority for providing R&R assistance as per Act.	Resolved		
2	12.04.2019	Saving of CPR (Temple)	The impact on structure is not much, the same was informed	Resolved		
3	06.05.2019	Enquiry about the exact location of acquisition	Details were provided by NHSRCL	Resolved		
4	14.05.2019	Regarding Land Acquisition in Kukkum Darshan Building	Details of the land to be acquired of concern region was provided.	Resolved		
5	04.06.2019	Land Acquisition details	Details were provided	Resolved		
