



QUARTERLY PROGRESS REPORT – IV (JULY – SEPTEMBER' 2019)

RAP Implementation Monitoring Format (Annexure M)

for

Mumbai – Ahmedabad High Speed Rail Limited

Submitted by:

NATIONAL HIGH SPEED RAIL CORPORATION LIMITED 2nd FLOOR, ASIA BHAWAN, ROAD NO-205,
DWARKA SECTOR 9, NEW DELHI – 110077

Quarterly Progress Report - 4


Time-Frame: 1st July' - 30th September, 2019

PROJECT AT GLANCE

The Ministry of Railways formulated the Indian Railways Vision 2020 in December 2009. The vision aims to modernize the existing conventional lines and enhance their traffic capacity as well as develop high-speed railway lines. Seven routes were selected as candidates for the high-speed railway system. Among them, the Mumbai–Ahmedabad route was given top priority by the Experts Committee on Modernization of India’s National Railways established by the Ministry of Railways. Based on this plan, the Mumbai–Ahmedabad High-Speed Railway will be implemented. In this context, Japan and India issued a joint statement in May 2013 committing to conduct a joint study on the Project. Based on this decision, the Joint Feasibility Study for Mumbai–Ahmedabad High-Speed Railway Corridor was conducted from December 2013 to June 2015. Then, the Prime Ministers of Japan and India issued a joint statement in December 2015, agreeing to introduce the Shinkansen High-Speed Railway (HSR) System to the Mumbai Ahmedabad route

Figure 1: Route of Mumbai–Ahmedabad High-Speed Railway line

The Mumbai–Ahmedabad High-Speed Railway Line (HSRL) will connect Mumbai, the capital city of Maharashtra and the second most populous metropolitan area in India, with Ahmedabad which is a metropolis in Gujarat. The approximately 508-km-long line will consist of high-speed railway running along the Arabian Sea coast and connecting with Surat and Vadodara en route which are the second and third largest city in Gujarat. The alignment will pass through Maharashtra, Gujarat and part in Dadra & Nagar Haveli covering 12 districts. The stretch in Maharashtra is 155.72 km, the stretch in Dadra & Nagar Haveli is 4.3 km and stretch in Gujarat is 348.15 km.

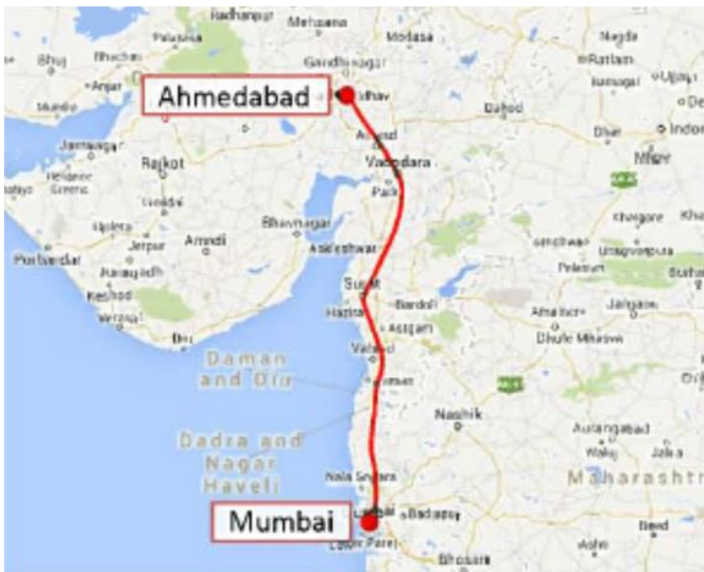

1. TOTAL LAND REQUIREMENT FOR THE PROJECT

In total, 1379.90 ha of land in 297 villages is required for the project. This includes private land, government land, forest land and land of Indian Railways. Around 72.81% of land plots affected are private land and remaining land belongs to Indian Railways, Government land and forest land.

2. KEY OBJECTIVE OF RESETTLEMENT ACTION PLAN

The main objective of the detailed resettlement action plan (RAP) is to ensure that the project design and implementation are socially acceptable based on the JICA Guidelines for Environmental and Social Considerations, 2010¹. From July, 2017 to July 2018, a Social Impact Assessment Study was done based on which a RAP has been prepared. The RAP is approved by NHRCL as per no. NHRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/2588 dated 12.09.2018. It has identified all potential social issues in the project and has developed mitigating measures for the impact of the project. The total estimated cost of implementing the RAP is ₹16,729.85 crores.

3. PROJECT IMPACT

The project being linear in nature is not expected to result in large-scale displacement of community. Impact on livelihood is mainly due to the acquisition of private agricultural land and business units along the project corridors. District-wise details of Project Impacts are presented in the table below.

SUMMARY OF PROJECT IMPACTS (As per RAP)	
➤	Total Number of Project Affected Household: 14,884
➤	Number of Affected Title Holder: 10,305
➤	Number of Affected Non-Title Holder: 4,579
➤	Total Number of Affected Structures: 3892
➤	Total Number of Affected CPRs: 37
➤	Total Number of Affected Commercial Structures: 271
➤	Total number of Impacted Trees on private land: 25,270

4. MONITORING OF RESETTLEMENT ACTION PLAN

From July, 2017 to July 2018, a Social Impact Assessment Study was done based on which a RAP has been prepared. The RAP is approved by NHRCL as per no. NHRCL/MA/CE01/JICAAPJTAPPRSL-TIGN/52.1/2588 dated 12.09.2018. It has identified all potential social issues in the project and has developed mitigating measures for the impact of the project.

NHRCL is submitting the fourth quarterly progress report to JICA for the period of July 1st, 2019 to Sep. 30th, 2019.

¹ https://www.jica.go.jp/english/our_work/social_environmental/guideline/pdf/guideline100326.pdf

KEY HIGHLIGHTS OF THIS QUARTER

1. Engagement of Staff for RAP Implementation: NHRCL has engaged human resources to cover this aspect at all three levels- Headquarters, Districts and Villages.

a. NHRCL's senior management along with Social Development Officer and Assistant Social Development Officer is in charge of matters at Headquarter level.

i. Managing Director	- 1
ii. Director (Projects)	- 1
iii. Officer on Special Duty	- 1
iv. Asst. General Manager (Procurement)	- 1
v. Social Development Officer	- 1
vi. Assistant Social Development Officer	- 1
vii. Project Managers (Civil)	- 1
viii. Project Managers (QAQC)	- 1

b. At the site 5 Chief Project Managers at Ahmedabad, Vadodara, Surat, Palghar and Mumbai are managing land acquisition and Resettlement Action Plan implementation related issues in Gujarat, Dadar & Nagar Haveli and Maharashtra. The details of staff deployed is given below.

S. No.	District	NHRCL			
		DILR/LAO's Office	Communicators	NHRCL's Staff	
				Permanent	Temporary/ Out-sourced Staff/Revenue
1	MUMBAI SUBURBAN	0	0	0	0
2	THANE	11	10	3	13
3	PALGHAR	92	0	19	41
4	DNH	0	0	0	1
5	VALSAD	5	17	5	10
6	NAVSARI	6	0	0	0
7	SURAT	8	8	2	5
8	BHARUCH	7	13	3	4
9	VADODARA	25	15	3	9
10	ANAND	7	4	1	4
11	KHEDA	8	8	1	9
12	AHMEDABAD	6	4	3	6
	Total	175	79	40	102

c. Through RAP implementing agency i.e. M/s Arcadis about 76 manpower has been deployed for land acquisition and social safeguard activities. Further, additional deployment of about 90 manpower has also been done by engaging two agencies i.e. CPMA and RANE for Information Education and Communication activities in Palghar district.

Details Provided in Row 1 of Attachment M

- 2. Progress of Joint Measurement Survey:** Out of total **297 villages** falling in the project alignment, field-work for JMS has been completed in **271 villages**. This is around 91 percent of the total villages. The other steps involved include preparation of Joint Measurement Reports for the villages, submission to district authorities and subsequent approval. **Approximately 89% of the Joint Measurement Reports** submitted to district administration have been approved by Land Acquisition Officer. Efforts are in place to expedite the process to complete the remaining stretch of JMS.

Details Provided in Row 2 of Attachment M

- 3. Valuation of Properties attached to the structure:**
Valuation has to be done for structures, trees and utilities attached to the land being acquired. After confirmation on numbers in Joint Measurement Report, the values of the structure is calculated by government authorized valuer. The details are further confirmed by Road & Building Department in Gujarat and Public Works Department in Maharashtra and DNH.

Details Provided in Row 3 of Attachment M

- 4. Verification of Impacts after completion of JMS**
NHSRCL created a software for Management Information System in March, 2019. After Joint Measurement Reports for the villages are finalized by the district administration, the complete details are filled in the software. While 14884 households were identified at the time of socio-economic survey during RAP, for the villages where JMS have been completed & JMR are received, the number of Project Affected Households are 9575 and corresponding number of project affected persons identified are 43249.

Details Provided in Row 4 of Attachment M

- 5. Adopting the RAP**
RAP has been summarized and translated into Gujarati and Marathi and the same has also been uploaded in NHSRCL Website. NHSRCL has also submitted a copy to all land acquisition officers. Further, communication campaigns are also been organized for Project Affected Persons (PAP).

Details Provided in Row 5 of Attachment M

- 6. Progress of Land Acquisition**
At present, NHSRCL is acquiring land on consent basis in both the states Maharashtra and Gujarat to reduce involuntary displacement. Consent camps are regularly organized to create awareness on the entitlement matrix & get final consent of the PAPs .

As per RAP, the total land requirement was 1434.47 hectares, however at present, total land requirement is 1,379.90 ha (148.99 ha governmental land, 127.50 ha railways land, 1004.73 ha private land, 98.68 ha forest land) as per approved JMR & initial Land Acquisition Plan for villages where JMR is yet to be prepared & approved. Till September 30th 2019, approximately 401.34 hectares of private land has been acquired through consent/direct purchase and in total (*comprising of Forest, Railways, Government and Private land*) 649.96 hectares of land has been acquired/transferred.

Details Provided in Row 6 of Attachment M

- 7. Income Restoration Programme (IRP) Assistance:** RAP implementation agency have undertaken “Training Need Assessment” surveys for identification of PAPs interested to enrol/undertake livelihood training. The trade of training/training plan are prepared after completion of training needs assessment survey. Income Restoration Plan for all district have been submitted to NHRCL by RAP implementation Agency. In last quarter (QPR-3) 28 candidate were enrolled in Computer Hardware and Networking programme and in the current quarter additional 63 candidates are undergoing training. Out of the total 63, 30 candidates are enrolled in Computer (Accounting), 19 candidates are enrolled in Computer (Hardware & Networking) and rest 14 candidates in Welding & Fabrication.
- 8. R&R award for Displaced Households:** R&R award in DNH has been declared by competent authority which includes 16 displaced families.
- 9. Relocation of Common Property Resources:** As on 30th September’ 2019 about 113 CPRs have been identified in the villages wherein JMS/JMR has been completed/submitted. During JMS ROW marking has been done on ground, based on the field survey new affected additional CPRs has been identified. Currently, NHRCL is in discussion with communities and land acquisition officers for relocation of common property resources.
- 10. Grievance Redress:** The RFCT-LARR 2013 has a mechanism of hearing grievances and objections by Collector/LAO’s at district level and all concern Collector/LAO’s are also resolving objections under Section-15 of the RFCT-LARR 2013. Thus, the State and District Administration may follow the same route without nomination of their representatives separately for District Level GRC.

However, NHRCL has established Level 1 (i.e. District Level Committee), Level 2 (i.e. Regional Level Committee) and Level 3 (i.e. Head Office Level Committee) Grievance Redressal Committee. NHRCL has also notified/ uploaded all GRC details in public domain (i.e. NHRCL Website). During the quarter 9 grievance were received in GRC and the same were resolved.
- 11. Details on Consent Camp:** During the quarter 319 no. of consent camp has been held and 69 no. of stakeholder and village level consultations has been held by RAP Implementation Agency.

Annexure M

MAHSR Project-RAP Implementation Monitoring Form

Attachment M

4th Quarter from July - September 2019

1 Progress of Land Acquisition and Resettlement													
Sl. No.	Activity	Unit	Planned Total	Progress in Quantity			Progress in %			Expected Date of Completion	Remarks	Implementing Party	
				During the Quarter	Till the Last Quarter	Up to the Quarter (Total Progress)	Till the Last Quarter	Up to the Quarter (Total Progress)					
1	Recruitment, training and deployment	1	Setting up SEMU and placement of staff	Person-month	15X8=120	404X3=1212	2562	3774	2135	3145	Complete/ In-progress	1. Total Planned = As per page 149 in RAP institutional arrangement 2. Details of Manpower deployed for Land Acquisition and Social work NHSRCLHO - 8 Field Units - 396 3. To expedite the land acquisition process additional manpower has been deployed in DILR/LAO Office. Further, RAP implementation agency and IEC agency are also engaged.	NHSRCL
		2	Deployment of RAP implementing human resource/ implementing NGOs by Arcadis at the site	Person-month	180	76X3=228	750	978	417	543	Complete/ In-progress	1.Total Planned = 180 person month as per RAP implementation agency contract document. 2. In total 79 manpower is engaged in RAP Implementation Agencies and it is likely to increase next month onwards. 3. No. of manpower engaged by Arcadis = 76 (Details listed below) Maharashtra - 32 Gujarat & DNH. - 44 4.Additional resources of manpower (90) were added to expedite land acquisition process by engaging IEC (Information Education and Communication) agency like CPMA & RANE.	NHSRCL
		3	Deployment of specialist/local NGOs for preparing and implementing Income Restoration Plan	Number of NGO	9	1	1	2	11.11	11.11	In-progress	NGO are engaged CPM wise. Till the current quarter 9 NGO have been identified by RAP implementation agency for providing skill development training. Further, no. of NGO may also increase as per suggestion of RAP implementation agency.	NHSRCL
		4	Deployment of External Monitoring Agency (EMA)	Number of Agency	1	1	1	1	100.00	100.00	Complete	Monitoring and Evaluation Agency LOI issued on 18.12. 2018. Team Mobilization from 10.01.2019.	NHSRCL
2	Progress of Joint Measurement Survey	1	Number of villages for which Field work of Joint Measurement Survey is complete	Village	297	20	251	271	84.51	91.25	In-progress		NHSRCL
		2	Total length for which ROW Marking is completed	Km	481.97	13.3	425.0	438.3	88.18	90.94	In-progress		NHSRCL
		3	Total length for which field work Joint Measurement Survey is complete	Km	481.97	28.9	405.36	434.24	84.10	90.10	In-progress		NHSRCL
		4	Number of JMS Reports verified by Department of Land Records	Village	297	17	246	263	82.83	88.55	In-progress		NHSRCL
		5	Number of JMS reports approved by Land Acquisition Officer	Village	297	22	241	263	81.14	88.55	In-progress		NHSRCL
3	Valuation of Structures/Trees/Utilities	1	Valuation completed	No. of Structures	3892	684	6230	6914	160.07	177.65	In-progress	Planned Total = 3892 (As per RAP Pg. 15). JMS work is still in-progress, thus the total scope can not be determined. Thus, planned total is taken from RAP.	NHSRCL
		2	Valuation approved by Concerned Dept. (PWD/R&B etc.)	No. of Structures	3892	1714	4163	5877	106.96	151.00	In-progress	About 6914 no. of structures have been identified in the villages wherein JMS/JMR has been completed/submitted. Out of total 6914 structures, 39% structures falls under other category like borewell, water tank, boundary wall etc. and 61% comprise of residential and commercial structures.	NHSRCL
		3	Valuation approved by Land Acquisition Officer	No. of Structures	3892	3137	2740	5877	70.40	151.00	In-progress		NHSRCL
		4	Valuation completed	No. of Trees	25270	9027	19092	28119	75.55	111.27	In-progress	Planned Total = 25270 (As per RAP Pg. 18). JMS work is still in-progress, thus the total scope can not be determined. Thus, scope is taken from RAP.	NHSRCL
		5	Valuation approved by Concerned Dept. (PWD/R&B etc.)	No. of Trees	25270	8745	17065	25810	67.53	102.14	In-progress		NHSRCL
		6	Valuation approved by Land Acquisition Officer	No. of Trees	25270	8745	15790	24535	62.49	97.09	In-progress		NHSRCL
		7	Valuation completed	No. of Utilities	169	48	75	123	44.38	72.78	In-progress	1.Planned Total = 169 (As per RAP Pg. 16). JMS work is still in-progress, thus the total scope can not be determined. Thus, scope is taken from RAP. 2.Borewell, Toilet, Water Tank, Tube Well, Well, Handpump are considered as Utility.	NHSRCL
		8	Valuation approved by Concerned Dept.	No. of Utilities	169	35	58	93	34.32	55.03	In-progress		NHSRCL
		9	Valuation approved by Land Acquisition Officer	No. of Utilities	169	35	33	68	19.53	40.24	In-progress		NHSRCL
4	Verification of Impacts after completion of JMS	1	Filling of data into NHSRCL's internal management information system(MIS)	No. of village	297	26	245	271	82.49	91.25	In-progress		NHSRCL
		2	Number of project affected household identified	No. of PAHs	14884	105	9470	9575	63.63	64.33	In-progress	No. of PAH has been identified based on JMR Report.	NHSRCL
		3	Number of project affected people identified	No. of PAPs	68048	305	42944	43249	63.11	63.56	In-progress		NHSRCL
		4	Number of people identified for relocation	No. of PAHs	1887	400	1454	1854	77.05	98.25	In-progress	Planned Total = As per RAP No. of PAP's Displaced has been identified. However, consent survey is in-progress wherein PAH choice for relocation is to be determined i.e. PAH willing for Self Relocation or demanding project based relocation.	NHSRCL
		5	Identification of PAPs for training	No. of PAPs	14884	552	734	1286	4.93	8.64	In-progress		NHSRCL
5	Adopting the RAP	1	Translation of RAP report into local language	No. of reports	2	2	2	100.00	100.00	In-progress	Planned Total = 2 (1 no. RAP Summary in Gujarati & 1 no. RAP Summary in Marathi). The translated version are uploaded in NHSRCL website.	NHSRCL	
		2	Organization of communication campaign for RAP awareness	No. of campaign	297	69	346	415	116.50	139.73	In-progress	Communication campaign are regularly organised. At times one village is been visited multiple times as consent is also in progress.	NHSRCL
6	Progress of Land Acquisition	1	Publication of Section 11 Notification	Village	297	60	200	260	67.34	87.54	In-progress	1. Earlier Section 11, 16, 19 & 21 is to be published for villages in Gujarat & DNH. However, now NHSRCL is acquiring land as per regular LA process for the State of Maharashtra as well. Thus, the above section will be published for Maharashtra state also.	NHSRCL
		2	Finalization of Micro-Plan	Village	297	12	0	12	0.00	4.04	In-progress		NHSRCL
		3	Publication of Section 16 Notification(Preparation of details)	Village	200	1	170	171	85.00	85.50	In-progress	2. Draft Micro Plan has been prepared for plots wherein Consent has been signed and JMR has been approved by LAOs. However, it is under review/verification by NHSRCL.	NHSRCL
		4	Publication of Section 19 notification	Village	200	7	169	176	84.50	88.00	In-progress		NHSRCL
		5	Publication of Section 21 notification	Village	200	41	126	167	63.00	83.50	In-progress		NHSRCL
		6	Publication of Namuna 1 Notification in Maharashtra	Village	97	0	97	97	100.00	100.00	Complete	Namuna 1 & 3 is to be published for Maharashtra	NHSRCL
		7	Publication of Namuna 3 Notification in Maharashtra	Village	97	13	46	59	47.42	60.82	In-progress		NHSRCL
7	Income Restoration Programme (IRP) Assistance	1	Number of Project Affected persons eligible/ identified for training	No. of PAPs	14884	552	734	1286	4.93	8.64	In-progress	PAPs identified for training in Gujarat & Maharashtra.	NHSRCL
		2	Number of training agencies identified	No. of Training Agency	5	1	1	2	20.00	40.00	In-progress	Training agencies has been identified for all districts.	NHSRCL
		3	Number of people undergone skill development training	No. of persons	14884	63	28	91	0.19	0.61	In-progress	Around 63 candidates are enrolled in training program of three different streams like Computer Hardware and Networking, Computer Accounting and Welding and Fabrication in Vadodara District.	NHSRCL
8	Relocation of Common Property Resources	1	Identification of CPRs to be relocated	No. of CPR	37	0	113	305.41	305.41	In-progress	Planned Total = 37 (As per RAP). About 113 CPRs have been identified in the villages wherein JMS/JMR has been completed/submitted. During JMS ROW marking has been done on ground, based on the field survey new affected additional CPRs has been identified.	NHSRCL	
		2	Number of CPRs relocated	No. of CPR	37	0	0	0.00	0.00	In-progress		NHSRCL	
9	Grievance Redress	1	Establishment of Grievance Redress Committees (GRCs)/Public complaint resolving Meetings	No. of GRCs	12	0	12	100.00	100.00	Complete	NHSRCL has established Level 1 (i.e. District Level Committee) with NHSRCL nominated officials, Level 2 (i.e. Regional Level Committee) and Level 3 (i.e. Head Office Level Committee) Grievance Redressal Committee. NHSRCL has also notified/ uploaded all GRC details in public domain (i.e. NHSRCL Website).	NHSRCL	
		2	Receiving complaints / claims form PAPs	No. of cases	43	9	34	43	79.07	100.00	In-progress	Grievances have been drastically reduced due to signing of consent agreement /direct purchase of land.	NHSRCL
		3	Responded complaints / claims	No. of cases	43	9	34	43	79.07	100.00	In-progress	All Grievance received during the quarter were resolved.	NHSRCL
10	Development of Resettlement sites	1	Resettlement/ relocation site identified	No. of sites	30	0	0	0.00	0.00	In-progress	Planned Total = 30 sites identified as per RAP	NHSRCL	
		2	Number of Project Affected Households shifted to temporary sites	No. of PAHs	1887	0	0	0.00	0.00	In-progress	Planned Total is as per RAP	NHSRCL	
		3	Co-ordination with different departments to provide basic amenities at proposed locations								In-progress	Not applicable in this quarter	NHSRCL
		4	Number of relocation/resettlement sites developed	No. of relocation sites							In-progress	Relocation Sites are being developed in consultation with District Administration.	NHSRCL
		5	Number of Project Affected Household relocated	No. of PAHs	1887	0	0	0.00	0.00	In-progress	At present No. of PAH's Displaced has been identified, their verification and document collection is in-progress. Further, also the consent survey is in-progress wherein PAH choice for relocation is to be determined i.e. PAH willing for Self Relocation or project assisted relocation. As of now it has been observed that majority of PAH are willing to take cash compensation for self-relocation.	NHSRCL	
11	Performance Reporting	1	Monthly Progress Report (submitted by Arcadis to NHSRCL)	No. of Reports	3	3	3	100.00	100.00	Complete		RAP Implementation Agency (Ms Arcadis)	
		2	Quarterly progress report (submitted by M&E Consultant to NHSRCL)	No. of Reports	1	1	0	1			In-progress	M&E Consultant mobilized from Jan,2019 onwards.	RAP M&E Agency (Ms CRADLE)
		3	Final Report (submitted by Arcadis to NHSRCL)	No. of Reports	1				0.00	0.00	In-progress		RAP Implementation Agency (Ms Arcadis)
		4	Submission of Quarterly progress report from NHSRCL to JICA	No. of Reports	4	1	3	4	75.00	100.00	In-progress		NHSRCL

2 Implementation of income restoration Assistance											
Brief Description of the implemented Income Restoration Program				Results during Report Period (No. of trainings implemented, No. of Participants, Etc)					Remarks		Location
Training program of three different streams like Computer Hardware and Networking, Computer Accounting and Welding and Fabrication				In total 63 candidates are undergoing training; 30 candidates are enrolled in Computer (Accounting), 19 candidates are enrolled in Computer (Hardware & Networking) and rest 14 candidates in Welding & Fabrication.					Training Provided by Team Lease Skill University, ITI Tarsali, Vadodara		Vadodara

3 Restoration of income and living Standard									
No	Date of Survey	Description about Surveyed Area	No. of Surveyed HHs	No. of PAHs with Increased incomes	No. of PAHs with Decreased incomes	No. of PAHs with Unchanged incomes	Types of Problems Encountered	Solution provided	Perceived Need for Additional Assistance
1									
2									
4 Details of Stakeholder Meetings									
S. No.	Date	Village/Tehsil/ District	Contents of the Consultation		Comments from Participants		Correspondences		
Gujarat									
1	06/07/19	Chainpur, Kali, Acher/ Ahmedabad	• Land Compensation • Rate Of Land		• PAPs who were satisfied with the information provided by NHRCL & State Authority proceeded for consent agreement		RAP Consultants		
2	13/07/19	Godasar, Vatva, RajpurHirpur, Ranip, Saherkotda, Geratpur/ Ahmedabad	• Resettlement & Rehabilitation Package		• In major section of Gujarat the rate declared by DLC were accepted by PAPs				
3	31/07/19	Asarva/ Ahmedabad	• Entitlement Matrix		• PAPPs appreciated the training prog. Of NHRCL and they also enquired about the details of training.				
4	03/08/19	Chainpur, Kali, Acher/ Ahmedabad	• Skill Development Training						
5	05/08/19	Vinzol, Ropda/ Ahmedabad	• Procedure for Consent Agreement						
6	21/08/19	Devdi/ Ahmedabad							
7	30/08/19	Barejdi, Devdi, Geratpur, Vinzol/ Ahmedabad							
8	04/09/19	Barejdi, Devdi, Geratpur, Vinzol / Ahmedabad							
9	05/09/19	Ghodasar, Khokhra, Saherkotda, Acher, Chenpur / Ahmedabad							
10	07/09/19	Ropda / Ahmedabad							
11	20/09/19	Kali / Ahmedabad							
12	21/09/19	Ropda/ Ahmedabad							
13	07/08/19	Manjalpur, Vadodara							
14	07/08/19	Kasba, Vadodara							
15	08/08/19	Manjalpur, Vadodara							
16	09/08/19	Sankarda Vadodara							
17	11/08/19	Chaklasi, Kheda							
18	12/08/19	Manjalpur, Vadodara							
19	13/08/19	Kasba, Vadodara							
20	13/08/19	Manjalpur, Vadodara							
21	14/08/19	Kasba, Vadodara							
22	14/08/19	Davda, Kheda							
23	14/08/19	Sankarda, Vadodara							
24	16/08/19	Kasba, Vadodara							
25	16/08/19	Davda, Kheda							
26	17/08/19	Ramnagar, Anand							
27	23/08/19	Chaklasi, Kheda							
28	19/08/19	Sankarda, Vadodara							
29	20/08/19	Sankarda, Vadodara							
30	23/08/19	Mahij, Kheda							
31	26/08/19	Adas, Anand							
32	30/08/19	Handod, Vadodara							
33	31/08/19	Vadsar, Vadodara							
34	31/08/19	Sankarda, Vadodara							
35		Chanvai/ Valsad/ Valsad (50)							
36		Dora/Amod/Bharuch (28)							
37		Kothi Vantars/Amod/Bharuch (20)							
MAHARASHTRA									
38	03/07/19	Kalher/Bhiwandi							
39	04/07/19	Betwade/Thane							
40	05/07/19	Aagasan/Thane							
41	11/07/19	Mhatardi/Thane							
42	18/07/19	Kharbhav/Bhiwandi							
43	18/07/19	Kalher/Bhiwandi							
44	19/07/19	Kharbhav/Bhiwandi							
45	22/07/19	Malodi/Bhiwandi							
46	07/08/19	Rambaug/Palghar							
47	07/08/19	Ambadi/Palghar							
48	08/08/19	Tembhi Khodave/Palghar							
49	07/08/19	Jalsar/Palghar							
50	01/08/19	Mhatardi/Thane							
51	06/08/19	Padle/Thane							
52	08/08/19	Davale/Thane							
53	12/08/19	Desai/Thane							
54	16/08/19	Shil/Thane							
55	21/08/19	Aagasan/Thane							
56	23/08/19	Betwade/Thane							
57	19/08/19	Paye/Bhiwandi							
58	20/08/19	Anjur/Bhiwandi							
59	06/09/19	Chari - Dahanu Taluka , Vevoor, Navli Palghar Taluka							
60	04/09/19	Kharbhav/Bhiwandi							
61	09/09/19	Malodi/Bhiwandi							
62	10/09/19	Kalher/Bhiwandi							
63	19/09/19	Kasheli/Bhiwandi							
64	06/09/19	Padle/Bhiwandi							
65	07/09/19	Usarghar/Thane							
66	11/09/19	Agasan/Thane							
67	19/09/19	Shil/Thane							
68	20/09/19	Betwade/Thane							
69	27/09/19	Desai/Thane							
5 Details of Grievance Redress									
No	Date of Receipts of Complaints	Contents of the Complaints			Action taken by NHRCL		Resolved / Not Yet Resolved		
1	10/07/19	Representation from Trust for exemption of acquisition of old heritage temple in Kuberpara, Bhilwas			NHRCL has taken serious note of the matter and the temple was exempted from acquisition.				
2	18/07/19	Representation of Agro Industry (Vadodara) for higher compensation			NHRCL has informed competent Authority to take note of the matter while determining compensation by LAO.		Resolved		
3	21/07/2019 & 26/09/2019	Housing Corp. (Vadodara) representation regarding acquisition of society common plot land			NHRCL has considered modified ROW to save society common plots and the matter was forwarded to competent authority (concern LAO) for consideration.		Resolved		
4	26/07/19	Grievance re regarding cutting of Mahogany trees for MAHSR Project			NHRCL has revised the design and ensured that, bare minimum trees will be affected. Further, compensatory afforestation in the ratio of 1:5 shall be done as per guidelines of Forest Dept.		Resolved		
5	29/07/19	Ownership Dispute regarding an affected plot in Vapi/Valsad			NHRCL has taken Cognizance of the matter and necessary corrections were made by the appropriate authority		Resolved		
6	01/08/19	Representation of Industry (Anand) for higher compensation			NHRCL has informed competent Authority to take note of the matter while determining compensation by LAO.		Resolved		
7	08/08/19	Representation of Packaging unit (Vadodara) for higher compensation			NHRCL has informed that, compensation amount shall be determined by competent Authority (i.e. Land Acquisition Officer) as per rule/act and NHRCL will honour and pay the compensation.		Resolved		
8	06/08/19	Adequate Compensation to People Affected due to MAHSR			NHRCL has informed that, compensation amount shall be determined by competent Authority (i.e. Land Acquisition Officer) as per rule/act and NHRCL will honour and pay the compensation.		Resolved		
9	06/09/19	Housing Society (Ahmedabad) requested to provide land in lieu of land under acquisition			NHRCL has informed that, project is linear in nature and the provision of land for land is not applicable for this project.		Resolved		
